


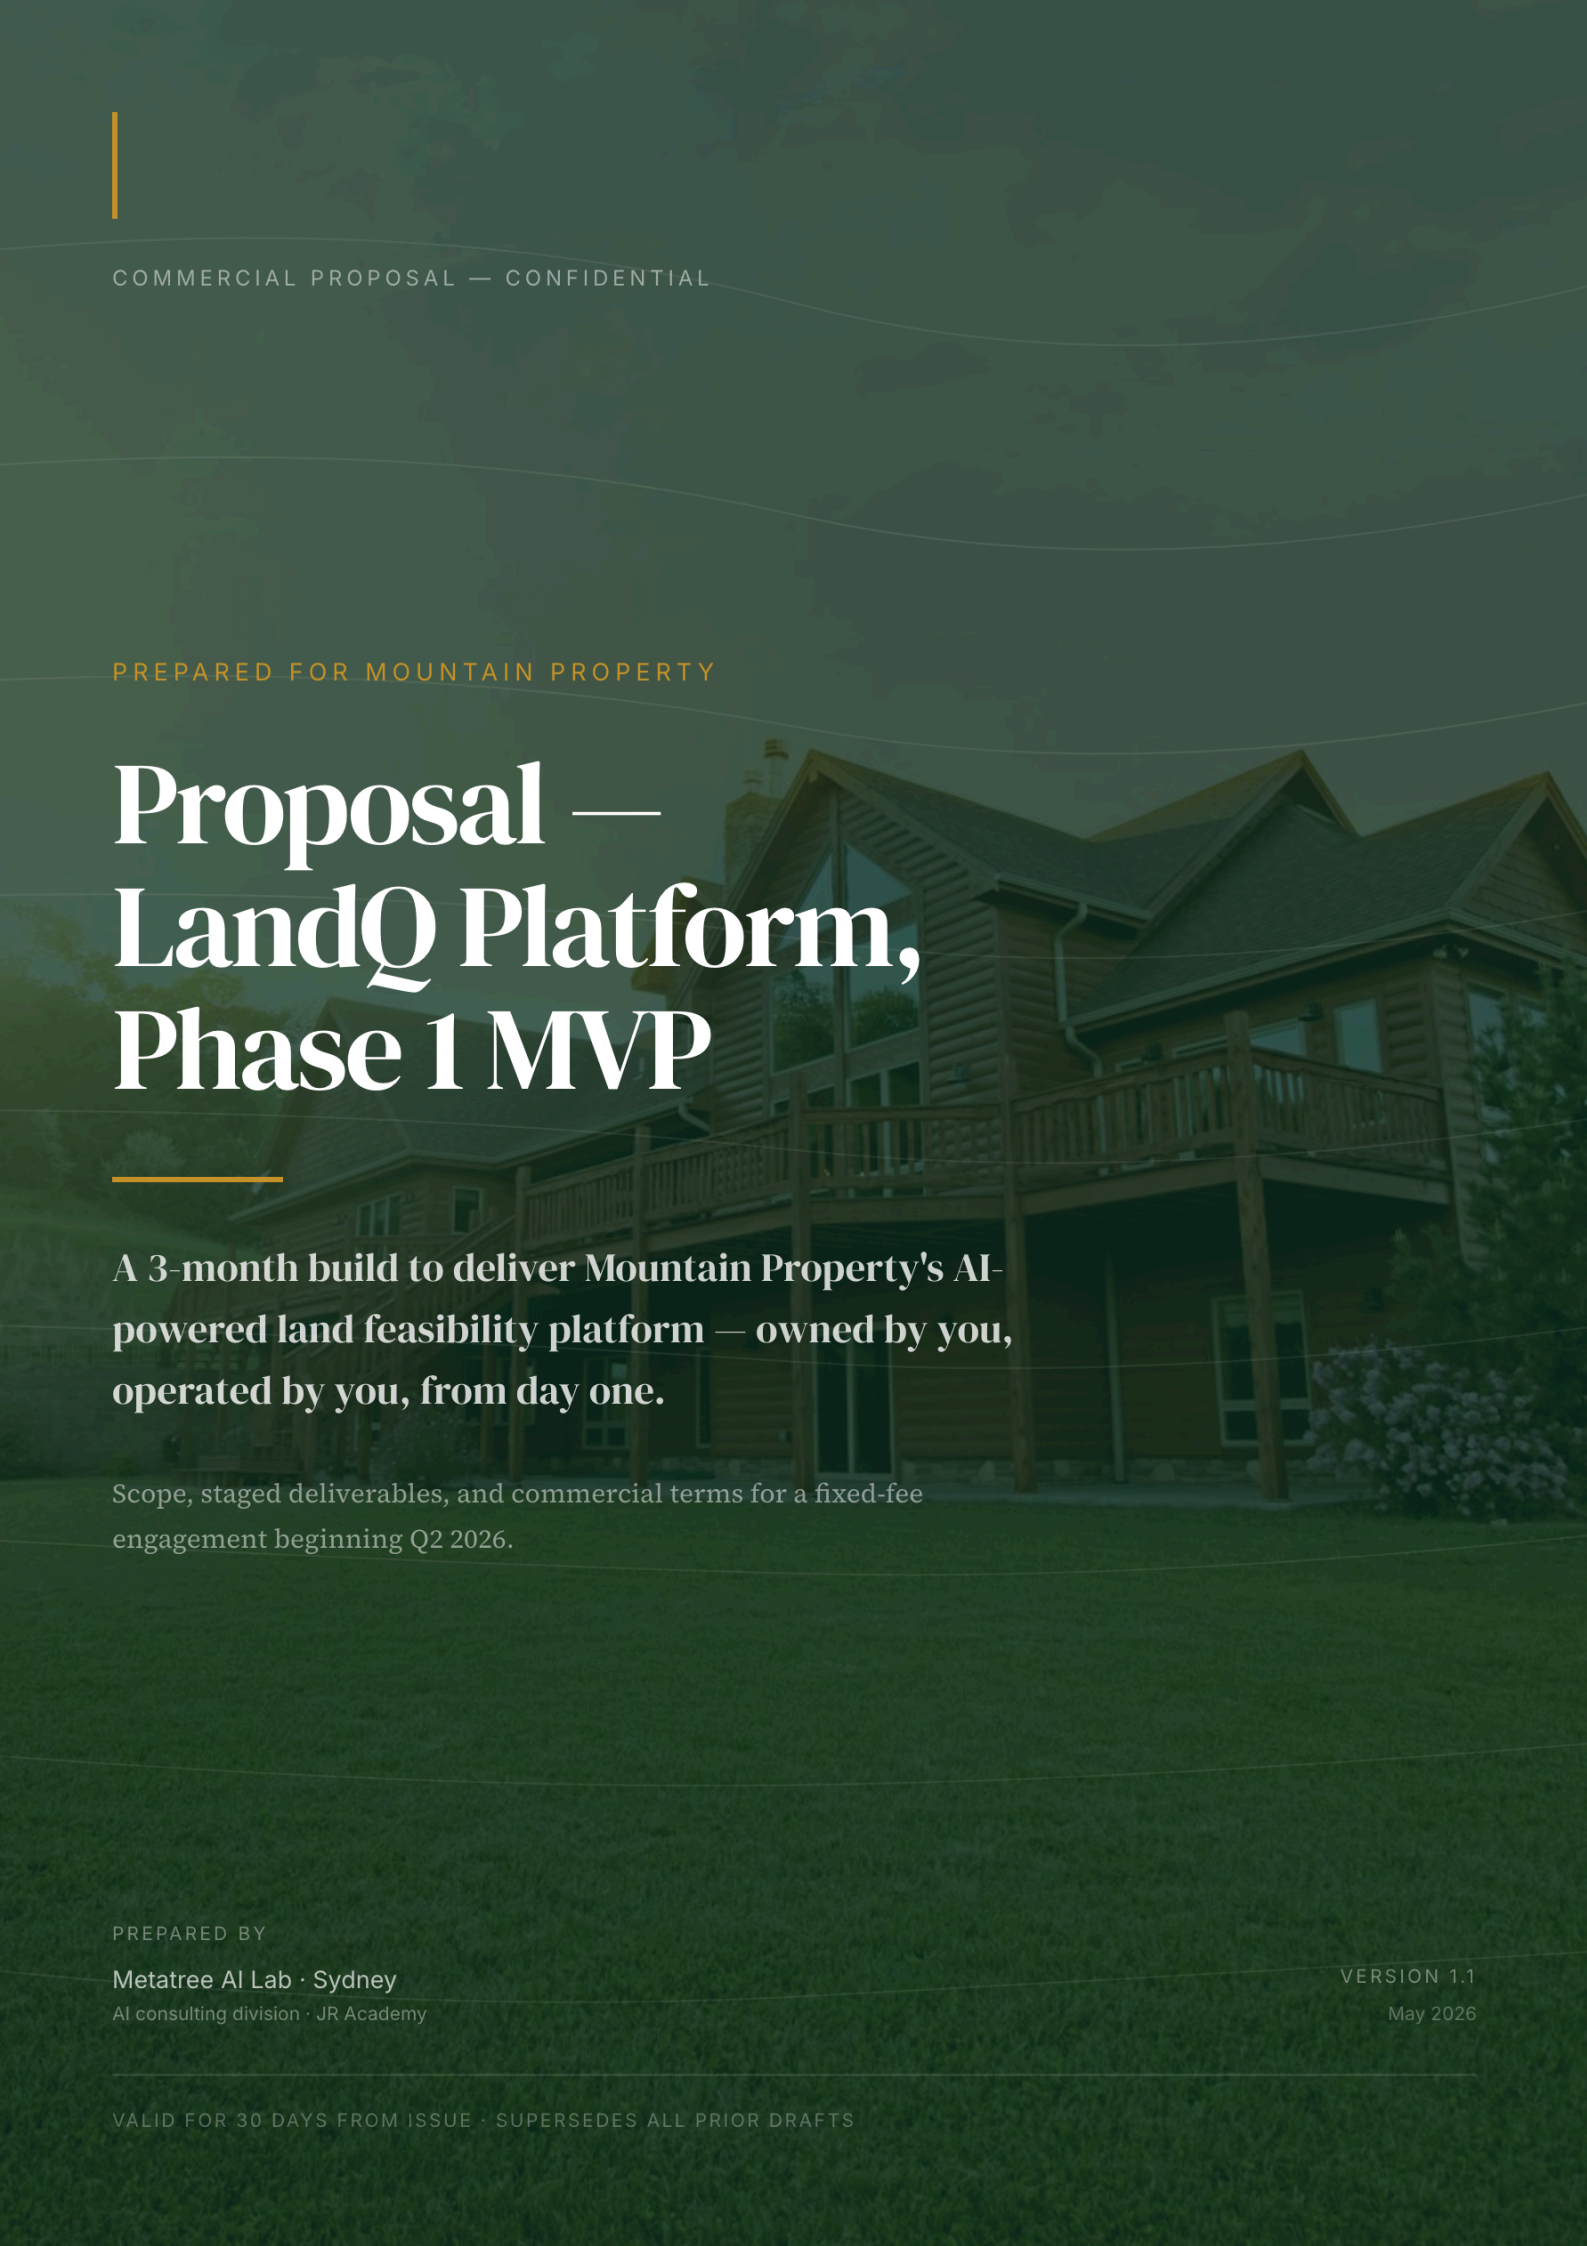

COMMERCIAL PROPOSAL — CONFIDENTIAL

PREPARED FOR MOUNTAIN PROPERTY

Proposal — LandQ Platform, Phase 1 MVP

A 3-month build to deliver Mountain Property's AI-powered land feasibility platform — owned by you, operated by you, from day one.

Scope, staged deliverables, and commercial terms for a fixed-fee engagement beginning Q2 2026.

PREPARED BY

Metatree AI Lab · Sydney

AI consulting division · JR Academy

VERSION 1.1

May 2026

VALID FOR 30 DAYS FROM ISSUE · SUPERSEDES ALL PRIOR DRAFTS

EXECUTIVE SUMMARY

A fixed-fee build of the Phase 1 platform — delivered in 3 months, owned by Mountain Property.

This proposal sets out the scope, staged deliverables, and commercial terms for Metatree AI Lab to design, build, and hand over the LandQ Phase 1 MVP for Mountain Property. It is structured to give you clear visibility of progress, and control over each milestone before the next begins.

ENGAGEMENT	Fixed-fee build of the LandQ Phase 1 MVP for Mountain Property — a working, production-grade land feasibility platform.
DURATION	~13 weeks (3 months) · Q2 2026 start → Q3 2026 delivery
TOTAL INVESTMENT	AUD \$90,000 + GST · fixed price across 4 milestones
OWNERSHIP	All source code, AI prompts, platform data, and hosting accounts belong to Mountain Property. No licence, no lock-in.
MOUNTAIN PROPERTY EFFORT	One product owner + ~2 hrs / week review. Metatree AI Lab handles everything else end-to-end.

WHY THIS WORKS FOR MOUNTAIN PROPERTY

- ◆ AI-accelerated build — 3 months of focused output at a fraction of a traditional in-house rebuild.
- ◆ Domain-owned team — the Metatree AI Lab engineers behind the national LandQ research, now building for you.
- ◆ You own the asset — code, data and IP transfer to Mountain Property at each milestone sign-off.

Mountain Property funds a single, focused Phase 1 build — and walks away with a platform, a team relationship, and full control of the asset.

THE OPPORTUNITY

Mountain Property can own the tool that every serious developer will need — and start using it first.

Australia approves 200K+ DA applications per year against a \$12.5 trillion housing base. Every one of those decisions passes through the same broken manual feasibility workflow. Phase 1 replaces the most expensive and repetitive part of that workflow — the desktop screening that consumes most of what Mountain Property currently pays to consultants.

01

Fragmented planning data

Every site assessment pulls from 20+ government portals, council GIS layers, PDFs and spreadsheets — repeated every time.

02

Manual feasibility

A single desktop feasibility takes 2–4 weeks and \$20K–\$60K in consultant time before a site is even shortlisted.

03

High sunk cost on dead sites

70–80% of investigated sites are abandoned — with the full DD spend already written off.

04

No single operating system

Opportunities, emails, consultant packs and decisions live across drives, inboxes and personal folders.

PHASE 1 TURNS THIS INTO →

One address in. One AI-generated feasibility out. In minutes, not weeks.

~80%TARGET COST REDUCTION
ON DESKTOP DD**2–4 wks → <1 hr**

TURNAROUND PER SITE

\$100K+

WASTED PER ABANDONED SITE TODAY

National

COVERAGE AT PHASE 1 HANDOVER

SCOPE OVERVIEW

Four stages, 13 weeks, one platform.

Phase 1 is delivered as four discrete stages. Each stage has its own scope, acceptance criteria, and fixed payment milestone — Mountain Property only moves to the next stage once the previous is accepted.

01

AI Foundation

Login, operations console, document hub and AI Q&A — Mountain Property can use it day 1.

WK 1–4

- Auth, RBAC & Admin Console operations
- Document hub — upload, tag, version, search
- RAG pipeline + AI Q&A over your documents

02

National Data Engine

Any Australian address returns a full planning profile in under 1 second.

WK 5–7

- Live integrations: state planning portals + cadastre
- Zoning, FSR, height, heritage, flood, bushfire overlays
- Interactive map with layer controls

03

AI Feasibility Report

One-click AI report replacing the bulk of desktop consultancy.

WK 8–11

- LLM-generated institutional-style feasibility report
- ROI / development-margin calculation (IRR, gross yield, dev margin)
- Risk scoring + cited planning controls + recommendation

04

Launch & Handover

Mountain Property team trained, running live, fully independent.

WK 12–13

- Excel workbook integration — import & per-report ROI export
- Portal + Console polish, onboarding, SSO, UAT, production cut-over
- Training, handover pack, source-code transfer

STAGE DELIVERABLES (1 OF 2)

AI Foundation & Data Engine — what's in the first 7 weeks.

STAGE 01 · WEEKS 1 – 4

M1 · AUD \$25,000

AI Foundation — Auth, Ops, Documents & Q&A

Mountain Property can log in, manage the org, upload documents, and run AI Q&A over them on day one.

DELIVERABLES

- Login / register / password reset · JWT + refresh tokens · bcrypt
- 5-role RBAC (owner / admin / manager / member / viewer) + invitation flow
- Admin Console — users, orgs, audit logs, system config
- Document hub — folders, upload, AI auto-tagging, full-text search, versioning, sharing
- RAG pipeline — chunking, pgvector embeddings, retrieval API
- AI Q&A surface — chat over the uploaded document corpus with cited sources
- Multi-tenant data model + cloud infra (Postgres/PostGIS/pgvector, Redis, S3) on Mountain Property's account
- Monorepo + CI/CD + staging environment + Sentry error tracking

ACCEPTANCE

- ✓ Invite flow end-to-end; role enforcement demonstrable in Portal and Console
- ✓ Uploaded document is searchable and Q&A-ready within 2 minutes, with citations to source

STAGE 02 · WEEKS 5 – 7

M2 · AUD \$25,000

National Data Engine

Any Australian address returns a full planning profile in under 1 second.

DELIVERABLES

- National address → cadastral lot geocoding (G-NAF + state cadastre feeds)
- Live integrations against state planning portals (ArcGIS REST, WFS, OpenData)
- Coverage: zoning, FSR / density, height, heritage, lot size, bushfire, flood overlays
- Bronze / Silver / Gold medallion storage with pre-aggregated lot features
- Scheduled ingestion (Prefect) + retry/backoff + structured logging + data-residency in AU
- Interactive site-intelligence map (Leaflet + CartoDB tiles, layer toggles)

ACCEPTANCE

- ✓ 5 benchmark sites across multiple states return complete planning profiles under 1s p95
- ✓ Re-ingest for one state completes cleanly end-to-end

STAGE DELIVERABLES (2 OF 2)

AI Reports & Launch — weeks 8 to 13.

STAGE 03 · WEEKS 8 – 11

M3 · AUD \$30,000

AI Feasibility Report

One-click AI report replacing the majority of Mountain Property's desktop consultancy spend.

DELIVERABLES

- Feasibility report generator (Claude/OpenAI) with institutional-style template
- Report sections: site overview, planning controls, risk score, yield estimation, comps reference, ROI / development margin, recommendation
- ROI / feasibility calculation: IRR, gross development yield, development margin — driven by FSR × indicative sale price × indicative build cost, with explicit assumptions printed inline
- Consumes Stage 2 Data Engine + Stage 1 RAG corpus — every claim cited
- Prompt registry + evaluation harness (versioned, git-tracked)
- Export to PDF/DOCX with source references in every generated section

ACCEPTANCE

- ✓ Report accuracy ≥ 85% on a Mountain Property 5-site benchmark set
- ✓ ROI section reconciles within ±10% of Mountain Property's own manual workbook on the same benchmark sites (where workbook is shared)
- ✓ Average report generation time ≤ 60 seconds

STAGE 04 · WEEKS 12 – 13

M4 · AUD \$5,000

Launch & Handover

Mountain Property is running the platform live, with the internal team fully trained and independent.

DELIVERABLES

- Portal + Console polish, empty states, onboarding flow, SSO (Google workspace optional)
- Land pipeline (lead → research → feasibility → negotiation → acquired)
- Excel feasibility workbook integration — import Mountain Property's existing workbook structure into the platform; export each AI-generated report's ROI section back to a matching Excel layout for offline review and circulation
- UAT cycle with Mountain Property team + triage of blockers
- Production cut-over, monitoring dashboards, automated backups, runbooks
- Two half-day training sessions (admin + end-user) + recorded walkthroughs
- Full source-code transfer, documentation pack, credentials handover
- 30-day post-launch hypercare (bug fixes + critical support included)

ACCEPTANCE

- ✓ Platform live on Mountain Property's production domain
- ✓ Zero P1 defects open at handover · runbooks rehearsed with Mountain Property ops

COMMERCIAL TERMS

Fixed fee. Milestone-based. No surprises.

TOTAL PHASE 1 INVESTMENT

AUD \$90,000 + GST

Fixed price. 5 acceptance-gated milestones. No hourly over-runs; scope changes via written change order.

CODE	DELIVERABLE	PAYMENT TRIGGER	SHARE	AMOUNT
M0	Technical Solution Package	On execution of this proposal	~5.6%	\$5,000
M1	Stage 1 — AI Foundation	Acceptance of Stage 1 deliverables	~27.8%	\$25,000
M2	Stage 2 — National Data Engine	Acceptance of Stage 2 deliverables	~27.8%	\$25,000
M3	Stage 3 — AI Feasibility Report	Acceptance of Stage 3 deliverables	~33.3%	\$30,000
M4	Stage 4 — Launch & Handover	Production sign-off + handover	~5.6%	\$5,000
TOTAL Phase 1 build · ex-GST · payable against accepted milestones				\$90,000

INCLUDED IN FEE

✓ All engineering, design, and AI work described in stages 1–4

✓ Claude / OpenAI API usage during Phase 1 build

✓ Staging + production environments (on Mountain Property's cloud)

✓ 30-day post-launch hypercare after M4

OUT OF SCOPE (PHASE 1)

✗ Self-hosted / on-premise LLM deployment (cloud LLM APIs are in scope)

✗ Custom council DCP crawlers beyond 5 reference councils

✗ Mobile-native apps and construction-phase workflow tools

✗ Bespoke analytics or BI integrations beyond the standard report export

✗ Ongoing hosting and third-party API fees after handover (passed through at cost)

Ownership: all source code, AI prompts, embeddings, and platform data created during Phase 1 transfer to Mountain Property on payment. No residual licence or revenue-share.

OPTIONAL · GOVERNMENT FUNDING OPPORTUNITIES

Two funding levers that can substantially reduce Mountain Property's net outlay on Phase 1.

The engagement is designed and delivered as a genuine R&D program — purpose-built for the AusIndustry R&D Tax Incentive (RDTI) and for joint industry-university grant applications. Both levers are **optional** and **stackable**; neither changes the scope, timeline, or fixed fee already agreed.

01 PREPAY FOR FY25-26 R&D TAX INCENTIVE

Settle the full engagement before 30 June 2026 to keep the whole \$90,000 inside Mountain Property's FY25-26 RDTI claim.

Phase 1 engagement (ex-GST)	\$90,000
Estimated qualifying R&D spend	~\$90,000
Refundable tax offset (SME, <\$20M turnover)	43.5%
Indicative return to Mountain Property	~\$39,150

WHAT MOUNTAIN PROPERTY GETS

- ✓ 43.5% refundable tax offset on qualifying R&D expenditure
- ✓ Cash refund paid out regardless of MP's tax position
- ✓ Offset claimed via standard FY25-26 tax return

WHAT METATREE AI LAB PROVIDES AT NO EXTRA FEE

- ✓ Technical-activity dossier mapped to RDTI 'core' and 'supporting' activities
- ✓ Time-tracked engineering logs exportable to MP's tax advisor
- ✓ AusIndustry registration template + response to any clarification

Subject to MP's tax-advisor eligibility assessment + AusIndustry registration. Percentage shown is the SME rate for companies with aggregated turnover under \$20M.

02 UNIVERSITY RESEARCH PARTNERSHIP

Co-author the engagement with an Australian university as an industry-research collaboration — unlocks a second funding layer stackable on top of the RDTI above.

PARTNER NETWORK (VIA JR ACADEMY)

JR Academy — Metatree AI Lab's parent network — maintains active research relationships with Australian universities across computer science, AI, and data disciplines, and can nominate a co-investigator onto the engagement.

PROGRAMS THAT MAY APPLY

ARC Linkage Projects	~50:50
Research + industry co-funded, 2-5 year horizon	
CRC-P (Cooperative Research Centres — Projects)	1:1 matched
Industry-led short-term collaboration, up to \$3M	
Industry PhD Program	Stipend-funded
3-year embedded PhD, cost-effective research capacity	
NSW MVP Ventures	Up to \$50K
State grant for SME commercialisation	

WHAT METATREE AI LAB PROVIDES AT NO EXTRA FEE

- ✓ Partner university shortlist + warm introduction to the co-investigator
- ✓ Joint R&D project scope, methodology and milestones
- ✓ Full grant application drafted + submitted; grants paid direct to MP

Subject to grant eligibility, round timing, and university partner sign-on. MP's contribution to matched funding can largely be covered by in-kind staff time rather than additional cash outlay.

NEXT STEPS

One signature away from a platform you own.

The fastest path from here to a working platform is simple. Sign, receive the Technical Solution, and we begin.

- | | | |
|----|--|-----------------------|
| 01 | Review this proposal
Confirm scope, staging, and commercial terms with your internal team. | WEEK OF RECEIPT |
| 02 | Sign the SoW
Executed Statement of Works + signed cover of this proposal trigger kick-off. | +1 WEEK |
| 03 | Receive M0 — Technical Solution Package
Architecture, data flow, security and integration plan — A4 pack + walkthrough. Unlocks \$5,000 invoice. | +2 WEEKS |
| 04 | Stage 1 kick-off
Cloud accounts provisioned, team onboarded, Foundation build begins. | WEEK OF M0 ACCEPTANCE |

ACCEPTANCE

For Mountain Property

For Metatree AI Lab

Name · Title · Date

Name · Director · Date
